

Cliente Ejemplo S.A.

Roadmap de Transformación de IA

Parte 2: DevOps Lifecycle

ASSESSMENT	AI Maturity Assessment 2026 H1
INDUSTRIA	Financial Services / Insurance
FECHA DEL ASSESSMENT	2026-05-08
VERSIÓN DEL FRAMEWORK	1.0.0
GENERADO EL	2026-05-08
ALCANCE	Engineering Organization


Confidencial | Cliente Ejemplo S.A.

Índice

1. Resumen Ejecutivo	.
2. Roadmap de Transformación	.
2.1 Horizonte 1: Fundación (Meses 0-6)	.
2.2 Horizonte 2: Escala (Meses 6-18)	.
2.3 Horizonte 3: Transformación (Meses 18-36)	.
3. Recursos	.
4. Métricas de Éxito	.
5. Riesgos y Mitigaciones	.
6. Próximos Pasos Recomendados	.

1. Resumen Ejecutivo

Este documento presenta el roadmap de transformación para DevOps Lifecycle como parte del journey de AI-Native Software Delivery Maturity de Cliente Exemplo S.A.. El roadmap delinea las iniciativas estratégicas, esfuerzo y cronograma necesarios para evolucionar de la madurez actual del pilar (L1.5) al nivel-objetivo (L4.0) durante un período de 36 meses.

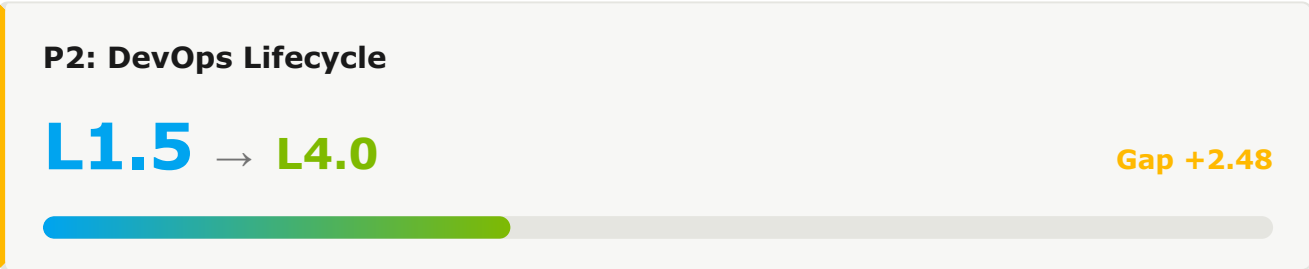

1.1 Evaluación del Estado Actual

MÉTRICA	VALOR ACTUAL	VALOR OBJETIVO	GAP
Deployment Frequency	Weekly	On-demand	Daily → On-demand
Lead Time for Changes	1-7 days	<1 hour	Significant
Change Failure Rate	15%	<5%	+10pp

1.2 Puntuaciones de Capabilities del Pilar 2

#	CAPABILITY	ACTUAL	OBJETIVO	GAP	PRIORIDAD
2.1	Source Control & Branching Strategy	L2.3	L3.0	0.7	(PRIORITY.P3)
2.2	PE CI/CD Pipelines	L0.0	L3.0	0.0	(PRIORITY.P3)
2.3	Build & Artifact Management	L2.4	L3.0	0.6	(PRIORITY.P3)
2.4	Test Automation	L0.8	L3.5	2.8	(PRIORITY.P0)
2.5	PE Security & DevSecOps	L0.0	L3.0	0.0	(PRIORITY.P3)
2.6	Release & Deployment Strategy	L0.0	L3.0	0.0	(PRIORITY.P3)
2.7	PE Observability & Monitoring	L0.0	L3.0	0.0	(PRIORITY.P3)
2.8	Incident Management & SRE	L0.0	L3.0	0.0	(PRIORITY.P3)
2.9	Chaos Engineering	L0.0	L3.0	0.0	(PRIORITY.P3)
2.10	Compliance & Audit Automation	L0.7	L3.0	2.3	(PRIORITY.P0)

2. Roadmap de Transformación

La transformación se desdobra en tres horizontes temporales — H1 (Fundación, Meses 0-6), H2 (Escala, Meses 6-18) y H3 (Transformación, Meses 18-36) — permitiendo construcción progresiva de capabilities mientras entrega valor incremental en cada etapa.

2.1 Horizonte 1: Fundación (Meses 0-6)

Objetivo: L1.5 → L2.5 · Establishing AI-Assisted Development Foundation

2.1 Source Control & Branching Strategy Actual: L2.3 → Objetivo H1: L2.5 · Gap: 0.2

EVIDENCIAS DEL ESTADO ACTUAL

- Mixed branching strategies
- Partial signed-commit enforcement

INICIATIVAS H1

- ✓ Standardize on trunk-based development
- ✓ Enforce branch protection org-wide
- ✓ Mandate signed commits across all repos

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
Trunk-based Repos	40%	85%

PE 2.2 CI/CD Pipelines

Actual: L0.0 → Objetivo H1: **L2.5** · Gap: 2.5

EVIDENCIAS DEL ESTADO ACTUAL

- 60% CD coverage
- Manual prod gates

INICIATIVAS H1

- ✓ Achieve 100% CD pipeline coverage
- ✓ Replace manual gates with automated checks
- ✓ Implement progressive delivery patterns

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
CD Coverage	60%	85%

2.3 Build & Artifact Management

Actual: L2.4 → Objetivo H1: **L2.5** · Gap: 0.1

EVIDENCIAS DEL ESTADO ACTUAL

- 50% SBOM coverage
- No reproducibility enforcement

INICIATIVAS H1

- ✓ Achieve 100% SBOM coverage
- ✓ Mandate reproducible builds
- ✓ Optimize build cache hit rates

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
SBOM Coverage	50%	100%

2.4 Test Automation

Actual: L0.8 → Objetivo H1: **L2.5** · Gap: 1.8

EVIDENCIAS DEL ESTADO ACTUAL

- 100% unit, 70% integration
- Manual flaky-test triage

INICIATIVAS H1

- ✓ Deploy automated flaky-test detection
- ✓ Move E2E tests to PR pipeline for critical paths
- ✓ Standardize test parallelization

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
Integration Coverage	70%	90%

PE 2.5 Security & DevSecOps

Actual: L0.0 → Objetivo H1: **L3.0** · Gap: 3.0

EVIDENCIAS DEL ESTADO ACTUAL

- 100% SAST/SCA
- 60% DAST
- Threat modeling pilot

INICIATIVAS H1

- ✓ Expand DAST to 100% of public services
- ✓ Roll out threat modeling tool org-wide
- ✓ Integrate AI vulnerability prioritization

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
DAST Coverage	60%	100%

2.6 Release & Deployment Strategy

Actual: L0.0 → Objetivo H1: **L2.5** · Gap: 2.5

EVIDENCIAS DEL ESTADO ACTUAL

- 30% canary
- 40% feature flags

INICIATIVAS H1

- ✓ Standardize feature flags across all services
- ✓ Expand canary deployments to 80% of services
- ✓ Automate rollback decisions based on SLO breaches

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
Canary Coverage	30%	70%

PE 2.7 Observability & Monitoring

Actual: L0.0 → Objetivo H1: **L3.0** · Gap: 3.0

EVIDENCIAS DEL ESTADO ACTUAL

- 80% tracing
- 70% SLOs
- Manual alerting

INICIATIVAS H1

- ✓ Deploy AI-driven anomaly detection
- ✓ Achieve 100% SLO coverage
- ✓ Reduce alert noise via intelligent grouping

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
SLO Coverage	70%	100%

2.8 Incident Management & SRE

Actual: L0.0 → Objetivo H1: **L2.0** · Gap: 2.0

EVIDENCIAS DEL ESTADO ACTUAL

- MTTR 30min-8h
- No SRE practice

INICIATIVAS H1

- ✓ Establish formal SRE function
- ✓ Standardize postmortem and action-item tracking
- ✓ Deploy AI-assisted incident triage

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
MTTR (P95)	8h	2h

2.9 Chaos Engineering

Actual: L0.0 → Objetivo H1: **L1.5** · Gap: 1.5

EVIDENCIAS DEL ESTADO ACTUAL

- No chaos practice
- Annual DR only

INICIATIVAS H1

- ✓ Deploy chaos engineering tooling
- ✓ Establish quarterly game day cadence
- ✓ Build chaos testing into pre-prod pipelines

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
Game Days/yr	0	4

2.10 Compliance & Audit Automation

Actual: L0.7 → Objetivo H1: L2.5 · Gap: 1.8

EVIDENCIAS DEL ESTADO ACTUAL

- 80% audit trail
- Partial compliance automation

INICIATIVAS H1

- ✓ Automate evidence collection for all controls
- ✓ Deploy continuous compliance dashboards
- ✓ Integrate compliance checks into CD pipelines

MÉTRICAS DE ÉXITO

MÉTRICA	ACTUAL	OBJETIVO H1
Automated Controls	60%	85%

2.2 Horizonte 2: Escala (Meses 6-18)

Objetivo: L2.5 → L3.0 · Scaling Platform Engineering & Agentic Workflows

Iniciativas Clave

IDP GENERAL AVAILABILITY

- ✓ Migrate all teams to IDP
- ✓ Establish golden paths for top 10 use cases
- ✓ Deploy AI-enhanced developer self-service

AGENTIC WORKFLOWS

- ✓ Roll out Agent Mode org-wide
- ✓ Deploy AI-driven pipeline optimization
- ✓ Implement AI test selection and prioritization

Objetivos de Capabilities — H2

CAPABILITY	SALIDA H1	OBJETIVO H2	HABILITADOR CLAVE
2.1 Source Control & Branching Strategy	L2.5	L3.5	AI-based PR routing
2.2 CI/CD Pipelines	L2.5	L3.5	AI-driven pipeline optimization
2.3 Build & Artifact Management	L2.5	L3.5	Distributed remote caching
2.4 Test Automation	L2.5	L3.5	AI test selection
2.5 Security & DevSecOps	L3.0	L3.5	AI-driven runtime protection
2.6 Release & Deployment Strategy	L2.5	L3.5	AI-driven release decisions
2.7 Observability & Monitoring	L3.0	L3.5	AI anomaly detection org-wide
2.8 Incident Management & SRE	L2.0	L3.0	AI-driven incident response
2.9 Chaos Engineering	L1.5	L2.5	Production chaos experiments
2.10 Compliance & Audit Automation	L2.5	L3.5	AI control attestation

2.3 Horizonte 3: Transformación (Meses 18-36)

Objetivo: L3.0 → L4.0 · Autonomous Operations and Self-Healing Systems

Iniciativas Clave

AUTONOMOUS SDLC

- ✓ Deploy multi-agent coding workflows
- ✓ Implement autonomous progressive delivery
- ✓ Achieve self-healing infrastructure

CONTINUOUS OPTIMIZATION

- ✓ AI-driven workload placement
- ✓ Predictive incident prevention
- ✓ Continuous compliance with AI verification

Objetivos de Capabilities — H3

CAPABILITY	SALIDA H2	OBJETIVO H3
2.1 Source Control & Branching Strategy	L3.5	L4.0 — Continuous integration with AI gating
2.2 CI/CD Pipelines	L3.5	L4.0 — Self-healing pipelines
2.3 Build & Artifact Management	L3.5	L4.0 — Hermetic builds with provenance
2.4 Test Automation	L3.5	L4.0 — Predictive test orchestration
2.5 Security & DevSecOps	L3.5	L4.0 — Autonomous security response
2.6 Release & Deployment Strategy	L3.5	L4.0 — Autonomous progressive delivery
2.7 Observability & Monitoring	L3.5	L4.0 — Predictive incident prevention
2.8 Incident Management & SRE	L3.0	L4.0 — Self-healing systems
2.9 Chaos Engineering	L2.5	L4.0 — Continuous chaos with AI safety net
2.10 Compliance & Audit Automation	L3.5	L4.0 — Continuous compliance with AI verification

3. Recursos

3.1 Inversiones en Tecnología

Las tecnologías abajo se recomiendan a lo largo del roadmap de 36 meses. El nivel de esfuerzo indica el costo de implementación de cada una — vea leyenda abajo.

TECNOLOGÍA	HORIZONTE	ESFUERZO	PROPÓSITO
Progressive Delivery Platform	H1	M	Canary + feature flags org-wide
AI Anomaly Detection	H1	M	Observability augmentation
Chaos Engineering Tooling	H2	S	Resilience validation
AI Pipeline Optimization	H2	M	Build/test/deploy intelligence
Self-Healing Pipelines	H3	L	Autonomous CI/CD

3.2 Equipo y Skills

ROL	FTES	HORIZONTE	FOCO
Platform Engineering Lead	1	H1	Pipeline strategy
SRE Engineers	4	H1	SRE function buildout
Security Engineers	2	H1	DevSecOps deepening
Platform Engineers	6	H2	Observability & chaos engineering

3.3 Resumen de Esfuerzo por Horizonte

HORIZONTE	DURACIÓN	ESFUERZO	ÁREAS DE FOCO
H1	0-6 months	M	Progressive delivery, SRE foundation
H2	6-18 months	L	Chaos eng, AI pipelines
H3	18-36 months	L	Self-healing operations
TOTAL	36 meses	L	Transformación completa de DevOps Lifecycle

LEYENDA DE NIVEL DE ESFUERZO

S

Pequeño

4-8 semanas · 2-3 FTE · 1 squad

M

Mediano

2-4 meses · 4-6 FTE · 1-2 squads

L

Grande

4-9 meses · 7-12 FTE · 2-3 squads

XL

Extra-Grande

9+ meses · 12+ FTE · cross-org

4. Métricas de Éxito

4.1 Evolución de Métricas DORA

MÉTRICA	ACTUAL	OBJETIVO H1	OBJETIVO H2	OBJETIVO H3
Deployment Frequency	Weekly	Daily	Multi-daily	On-demand
Lead Time for Changes	1-7 days	<1 day	<4 hours	<1 hour
Change Failure Rate	15%	10%	7%	<5%
MTTR (P95)	8h	4h	1h	<30 min

4.2 Métricas Operacionales

MÉTRICA	ACTUAL	OBJETIVO H1	OBJETIVO H2	OBJETIVO H3
SLO Coverage	70%	100%	100%	100%
Game Days/yr	0	4	12	Continuous
Incident MTTR	8h	2h	30min	<10min auto

5. Riesgos y Mitigaciones

RIESGO	IMPACTO	PROBABILIDAD	MITIGACIÓN
Pipeline disruption during transition	ALTA	BAJA	Staged rollout, parallel pipelines, automated rollback
Security regression with AI tooling	ALTA	BAJA	AI-aware security scanning, mandatory review, audit trails
Tool sprawl	MEDIA	MEDIA	Standardize on validated tool catalog, sunset legacy tools per quarter

6. Próximos Pasos Recomendados

6.1 Acciones Inmediatas (Próximos 30 Días)

- 1 Establish formal SRE function with named lead
- 2 Inventory existing pipeline maturity per service
- 3 Identify priority services for canary + feature flag rollout
- 4 Define SLO target framework
- 5 Procure progressive delivery tooling

6.2 Actividades de Lanzamiento H1 (Días 30-90)

- 1 Achieve 100% CI/CD pipeline coverage gap closure for prioritized services
- 2 Deploy AI anomaly detection to first 5 tier-1 services
- 3 Run first chaos engineering game day
- 4 Standardize postmortem template and tracking
- 5 Launch DevSecOps deepening initiative (DAST 100%, threat modeling)

6.3 Dependencias

- Part 1: Developer Productivity for AI test generation alignment
- Part 3: Application Platform observability stack alignment
